



TIME SQUARE 10 SHV REPORT

09.March.2026



TIME SQUARE 10 SHV LOCATION



TIME SQUARE 10 SHV LOCATION




TIME SQUARE 10 SHV ANOTHER POINT OF VIEW



TIME SQUARE 10 SHV FLOOR PLAN




SITE PROGRESS UP TO 09 MARCH 2026

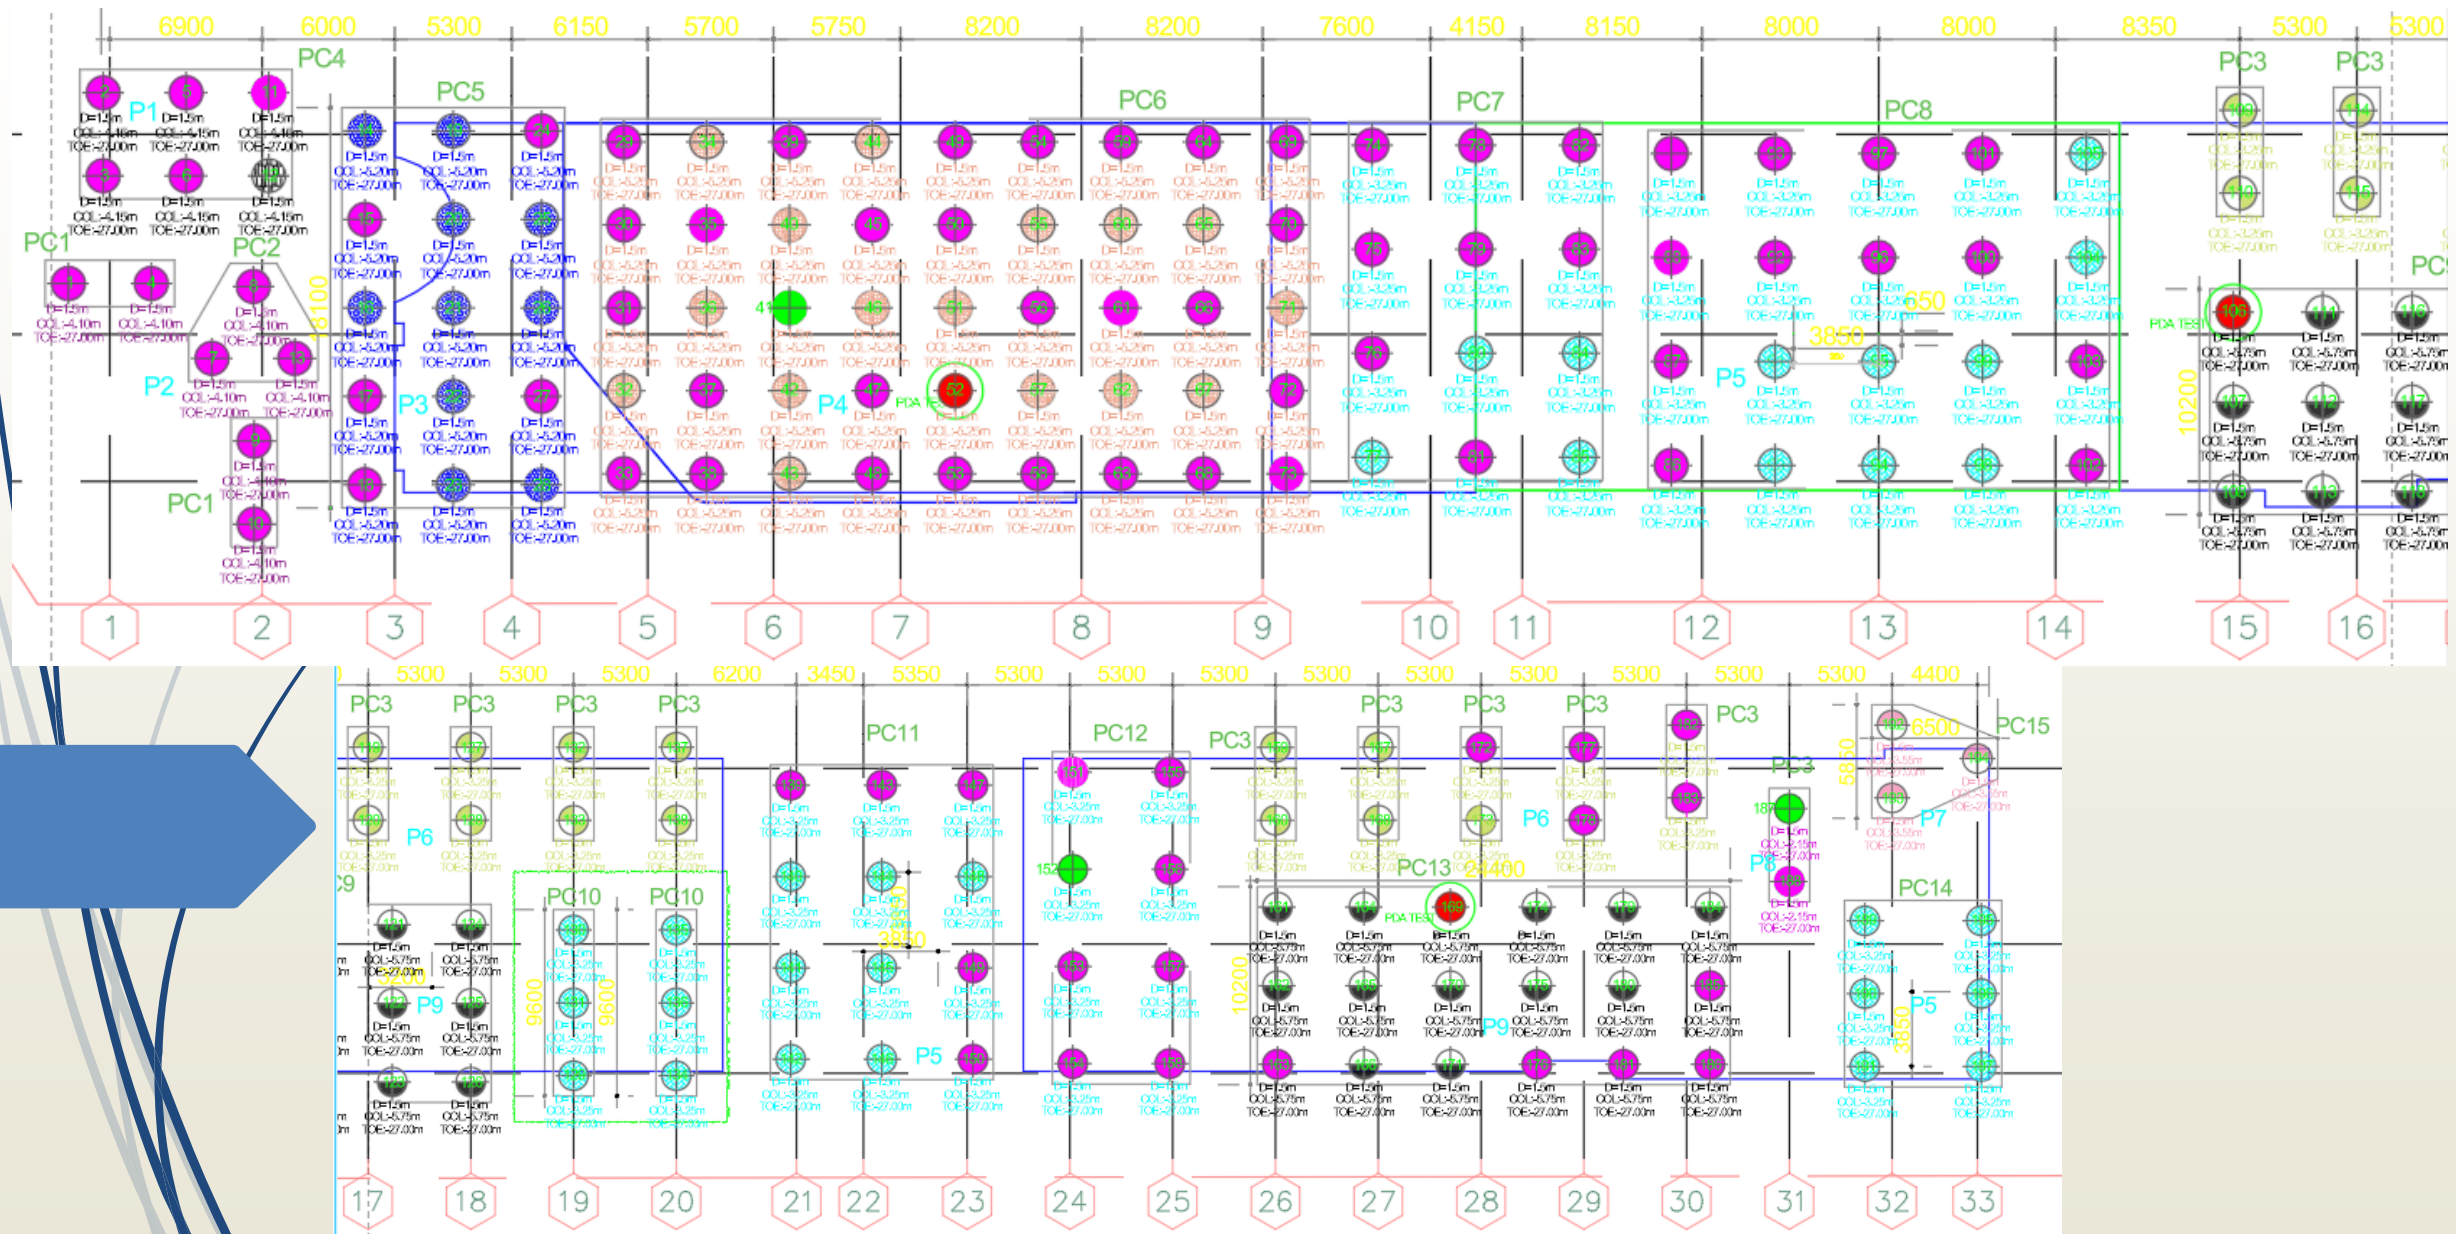

SITE PROGRESS UP TO 09 MARCH 2026

BORE PILE FINISHED 90/197p

Bored pile progressing

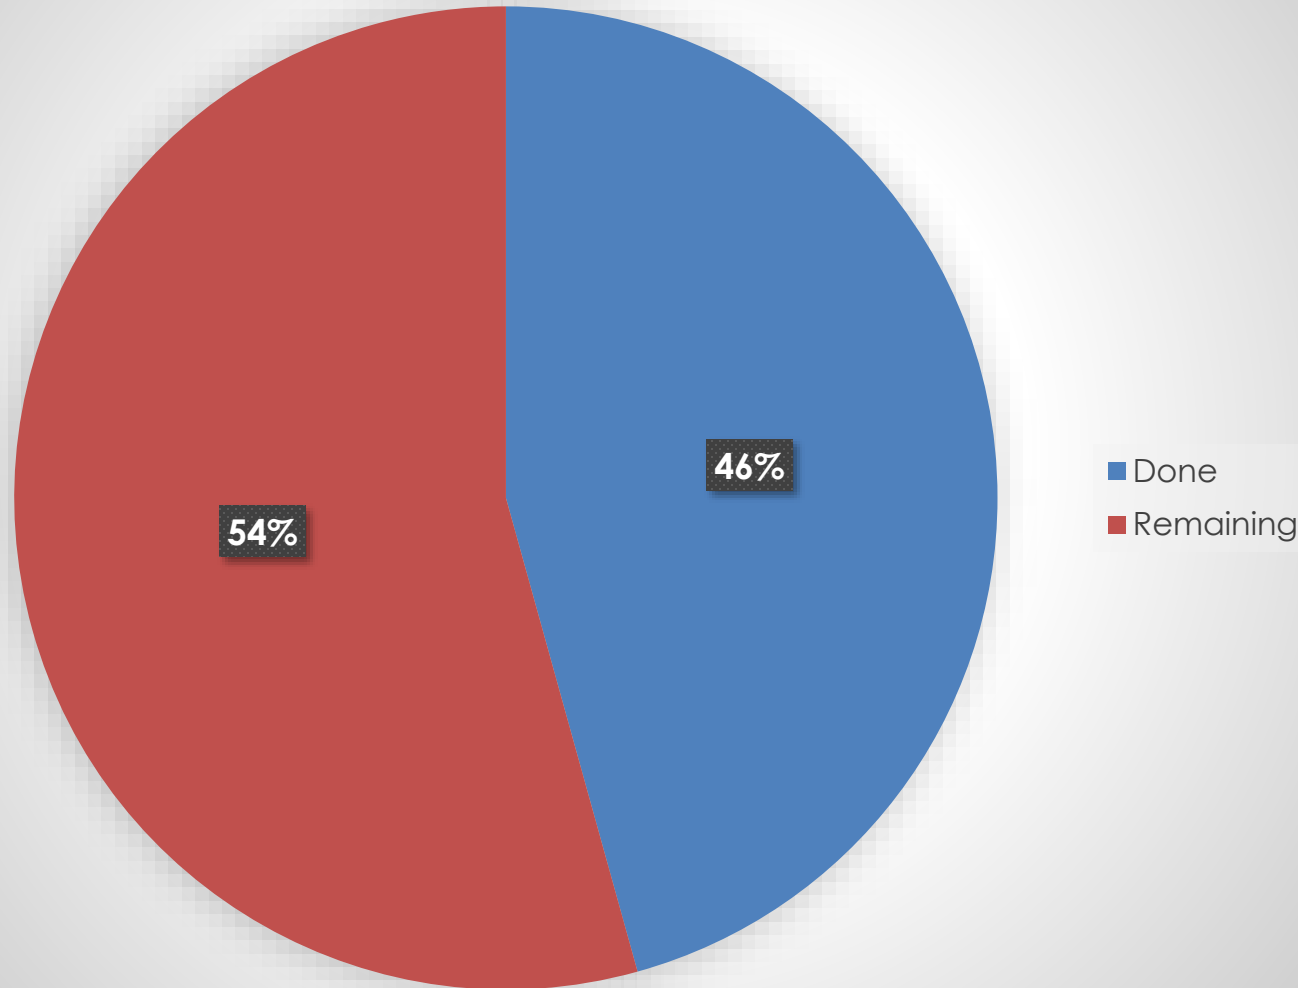

TOOL BOX MEETING



SURVEY INSPECTION



SURVEY INSPECTION



BORE PILE DRILLING



REBAR INSPECTION



REBAR INSPECTION



DEPTH INSPECTION BEFORE CONCRETE



PROJECT NAME	Time Square 10 SHV
Depth Inspection	Date 08/Nov/2026 Time 09:36
Pile Number	P-177
Design Depth	27.00m
Depth From TOC	29.10m
Status	Approved
Prepared By	FEK VIREAK
Approved By	
Diameter	1500mm
Top Casing	1.200m
Actual Depth	27.10m

INSTALLING REBAR BEFORE CONCRETE



BENTONITE SLURRY INSPECTION



BENTONITE SLURRY INSPECTION



CONCRETE INSPECTION




CONCRETE INSPECTION



CONCRETE 7DAYS STRENGTH TEST



CONCRETE 28DAYS STRENGTH TEST

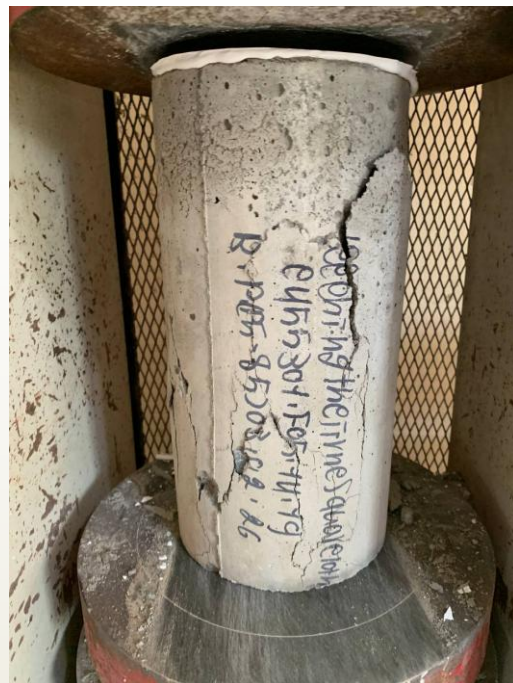

MATERIALS ARRIVED ON SITE



MATERIALS CONTROL



SITE CLEANING




CONSTRUCTION ENVIRONMENT





PASSION FOR PROGRESS!



TIME SQUARE 10 OCEAN VIEW

THE BEST DAY IN OTRES BEACH

THANK YOU!
