



TIME SQUARE 10 SHV REPORT

29 September 2026



TIME SQUARE 10 SHV LOCATION




TIME SQUARE 10 SHV LOCATION



TIME SQUARE 10 SHV ANOTHER POINT OF VIEW



TIME SQUARE 10 SHV FLOOR PLAN

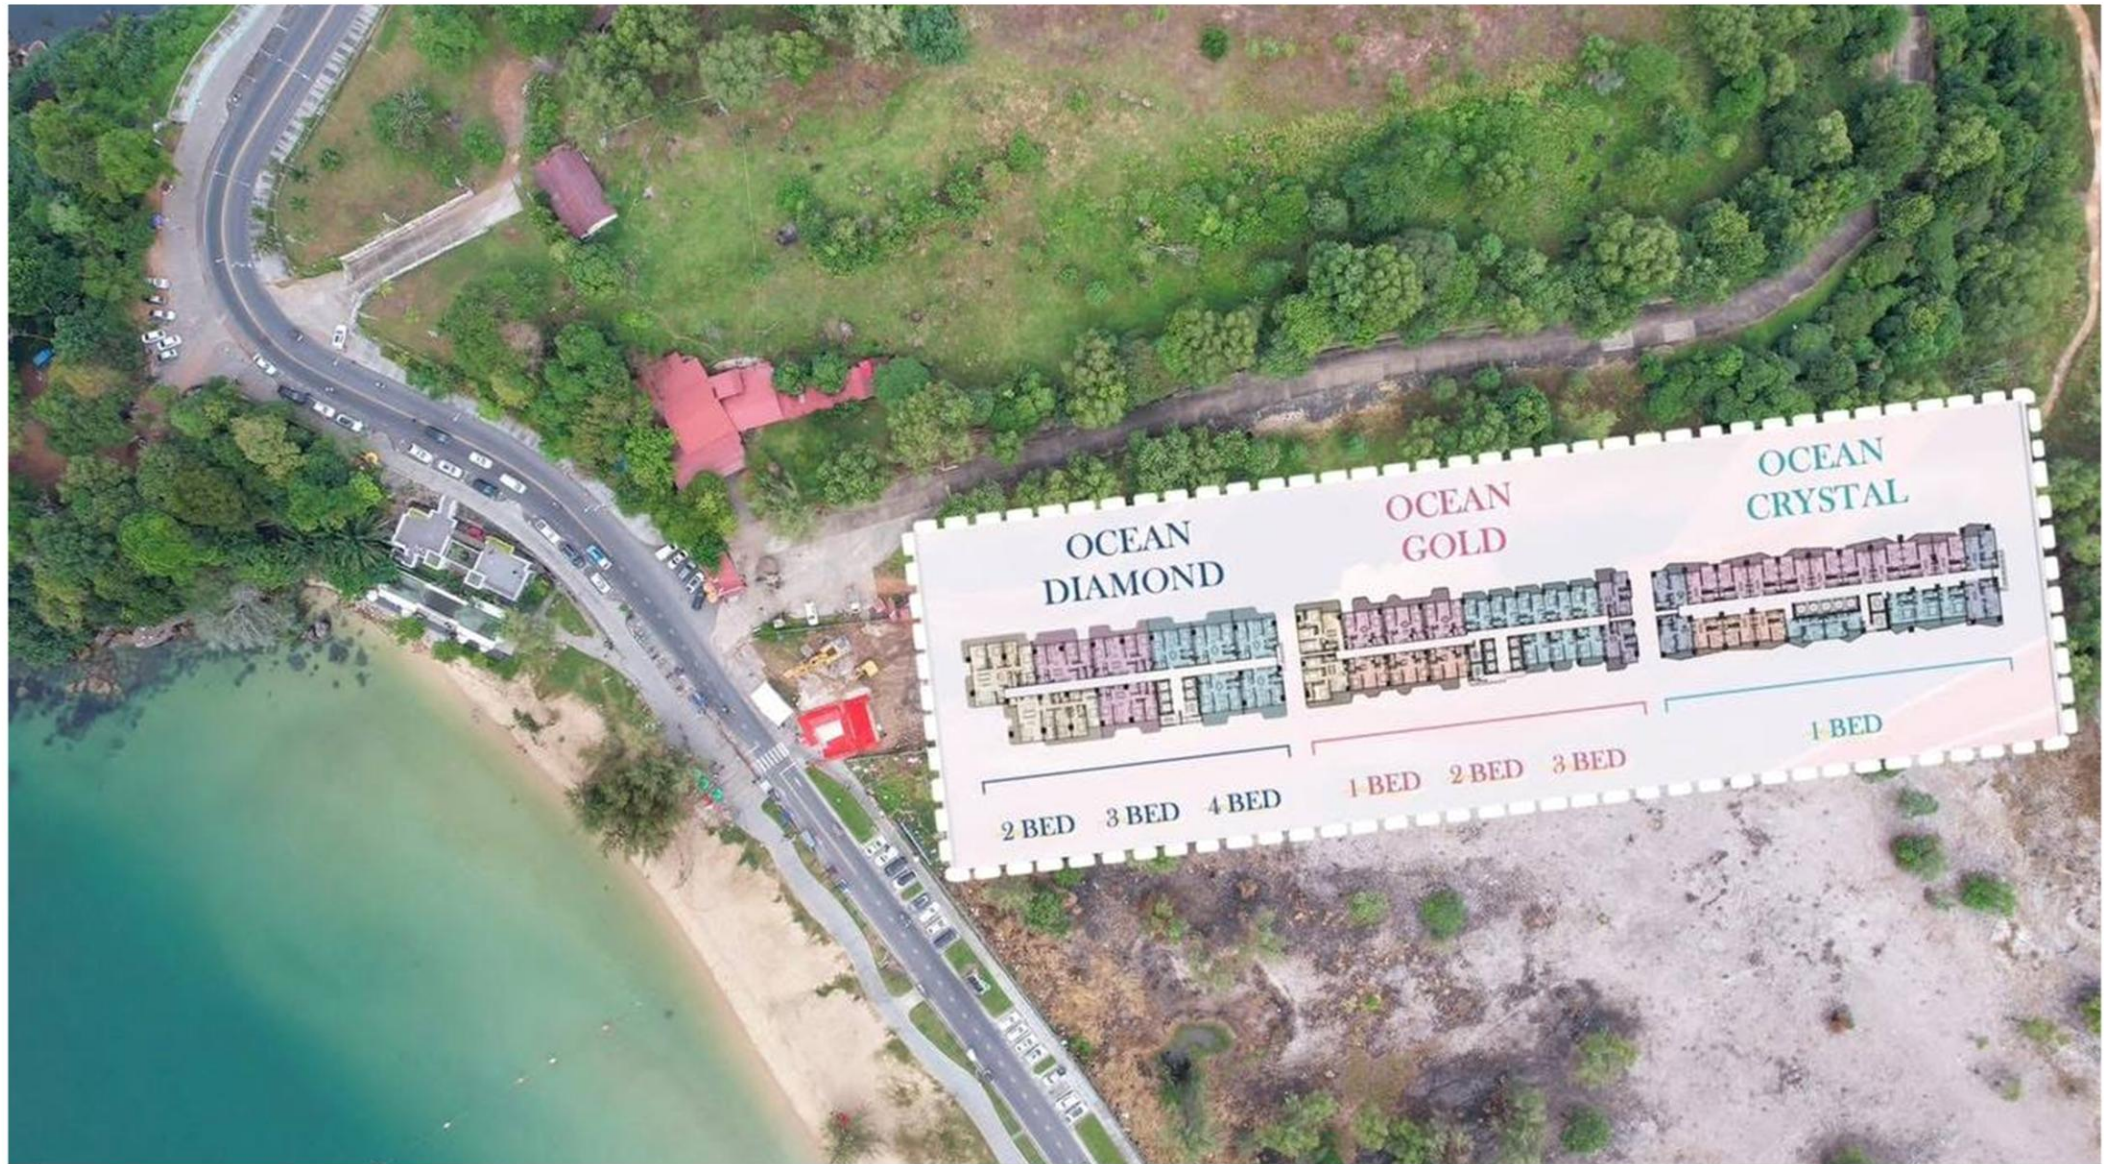

TOOL BOX MEETING




MEETING WITH CONCRETE TEAM




BREAKING PILE-HEAD PROGRESS UP TO 29 SEPTEMBER 2026


164/197pcs

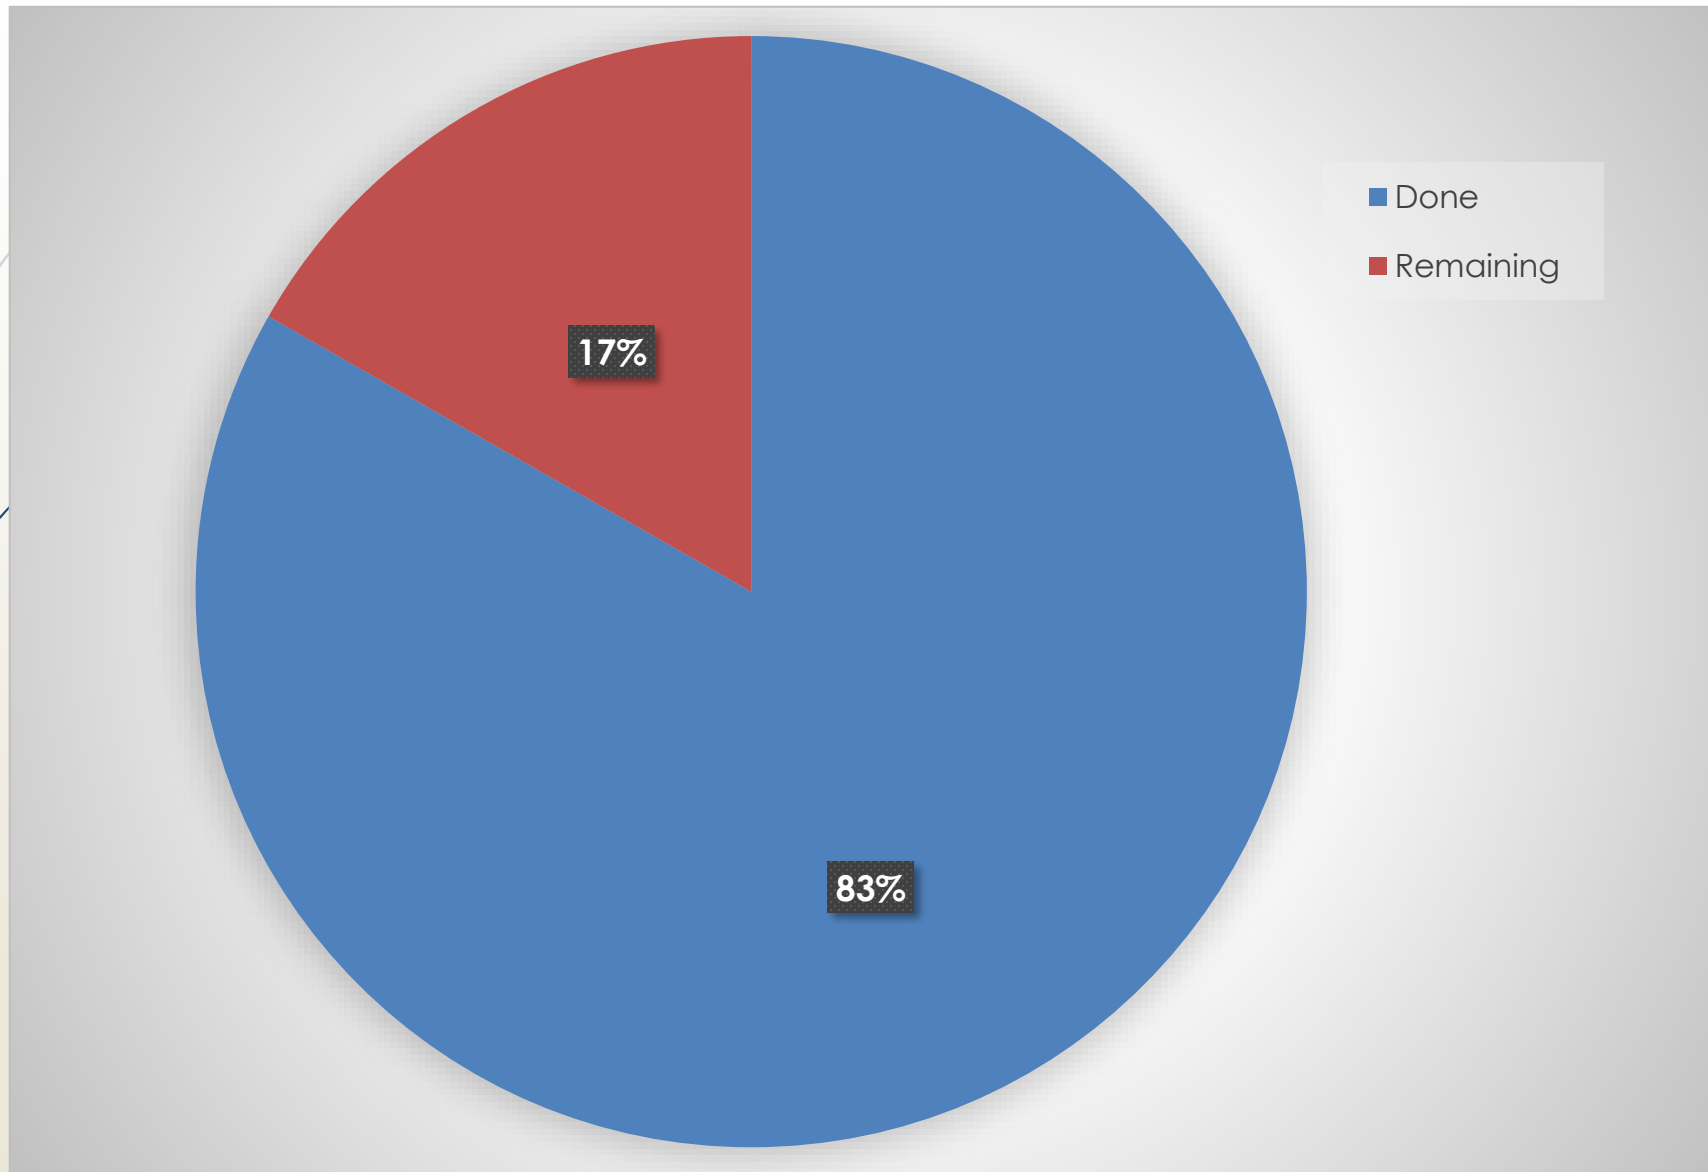

PILECAP FINISHED PROGRESS UP TO 29 SEPTEMBER 2026

20/28pc

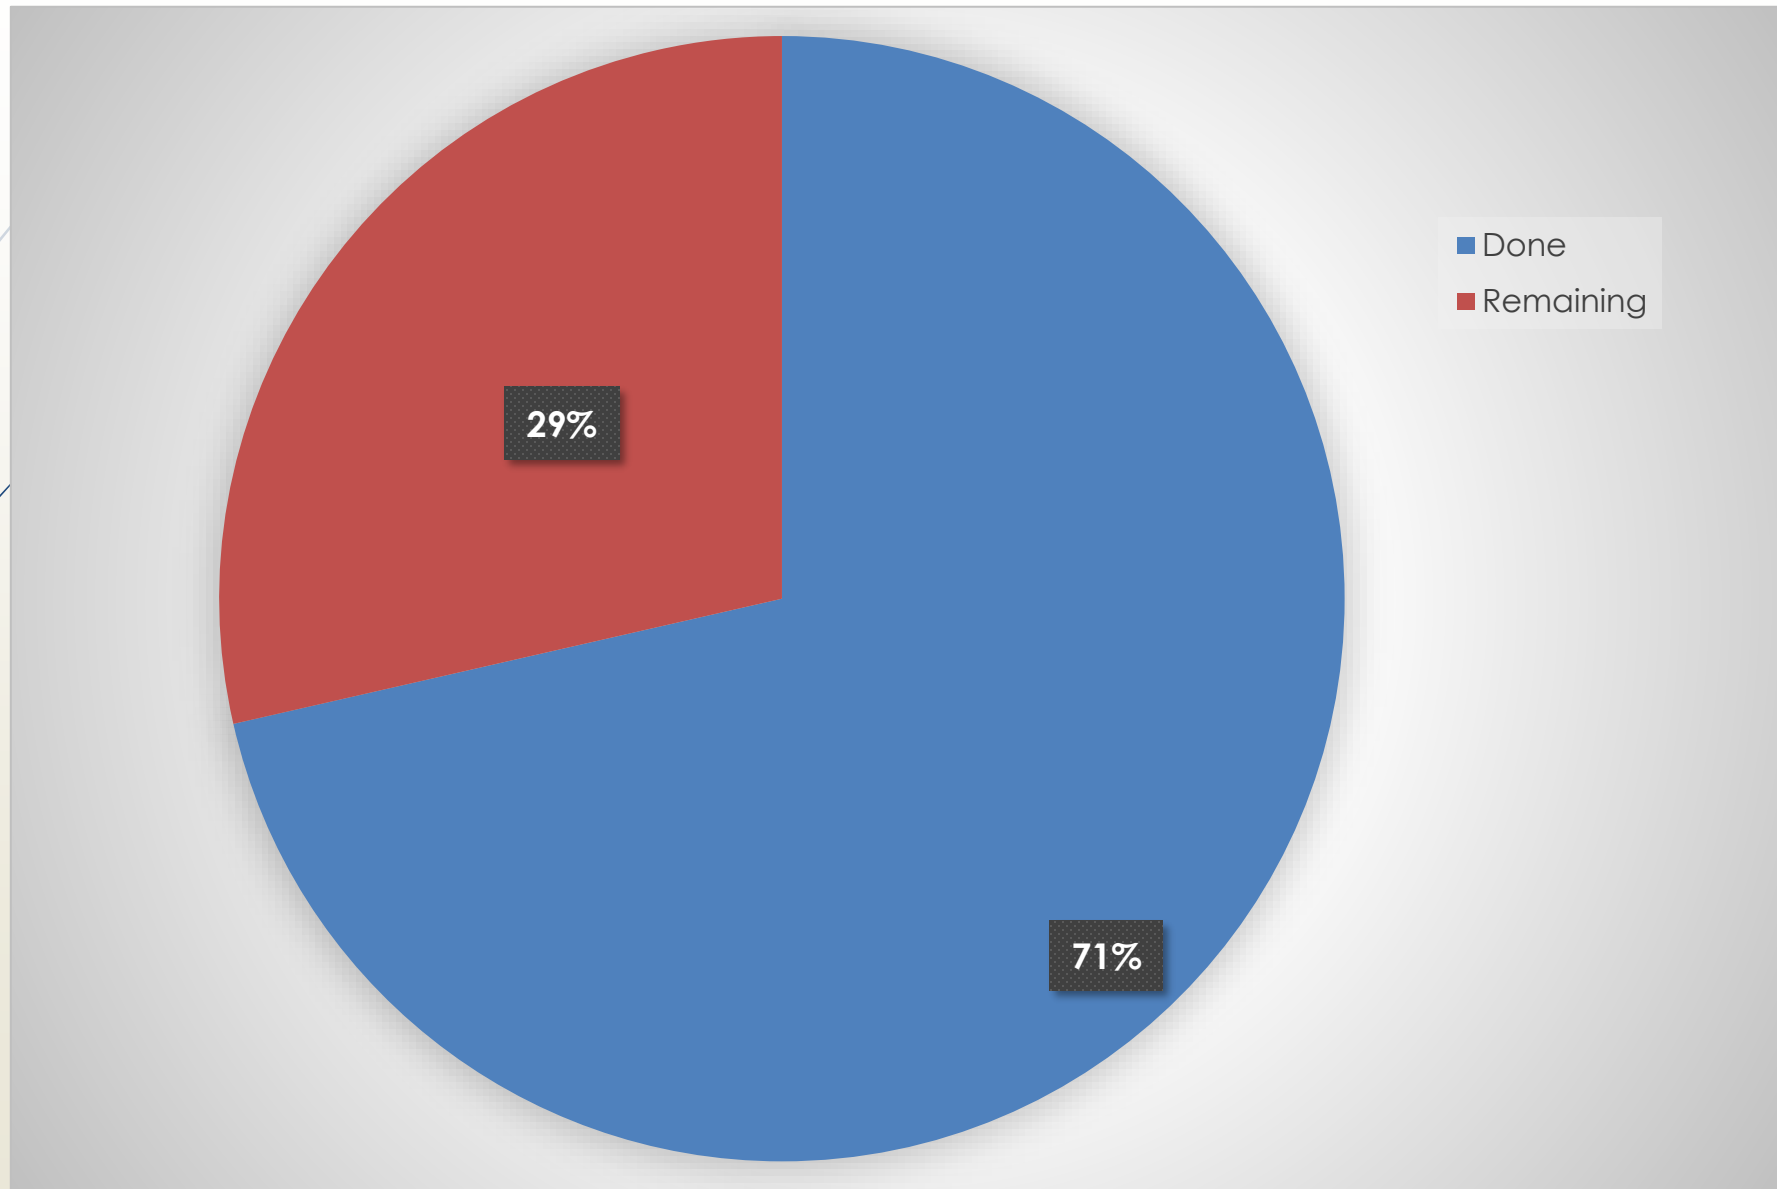

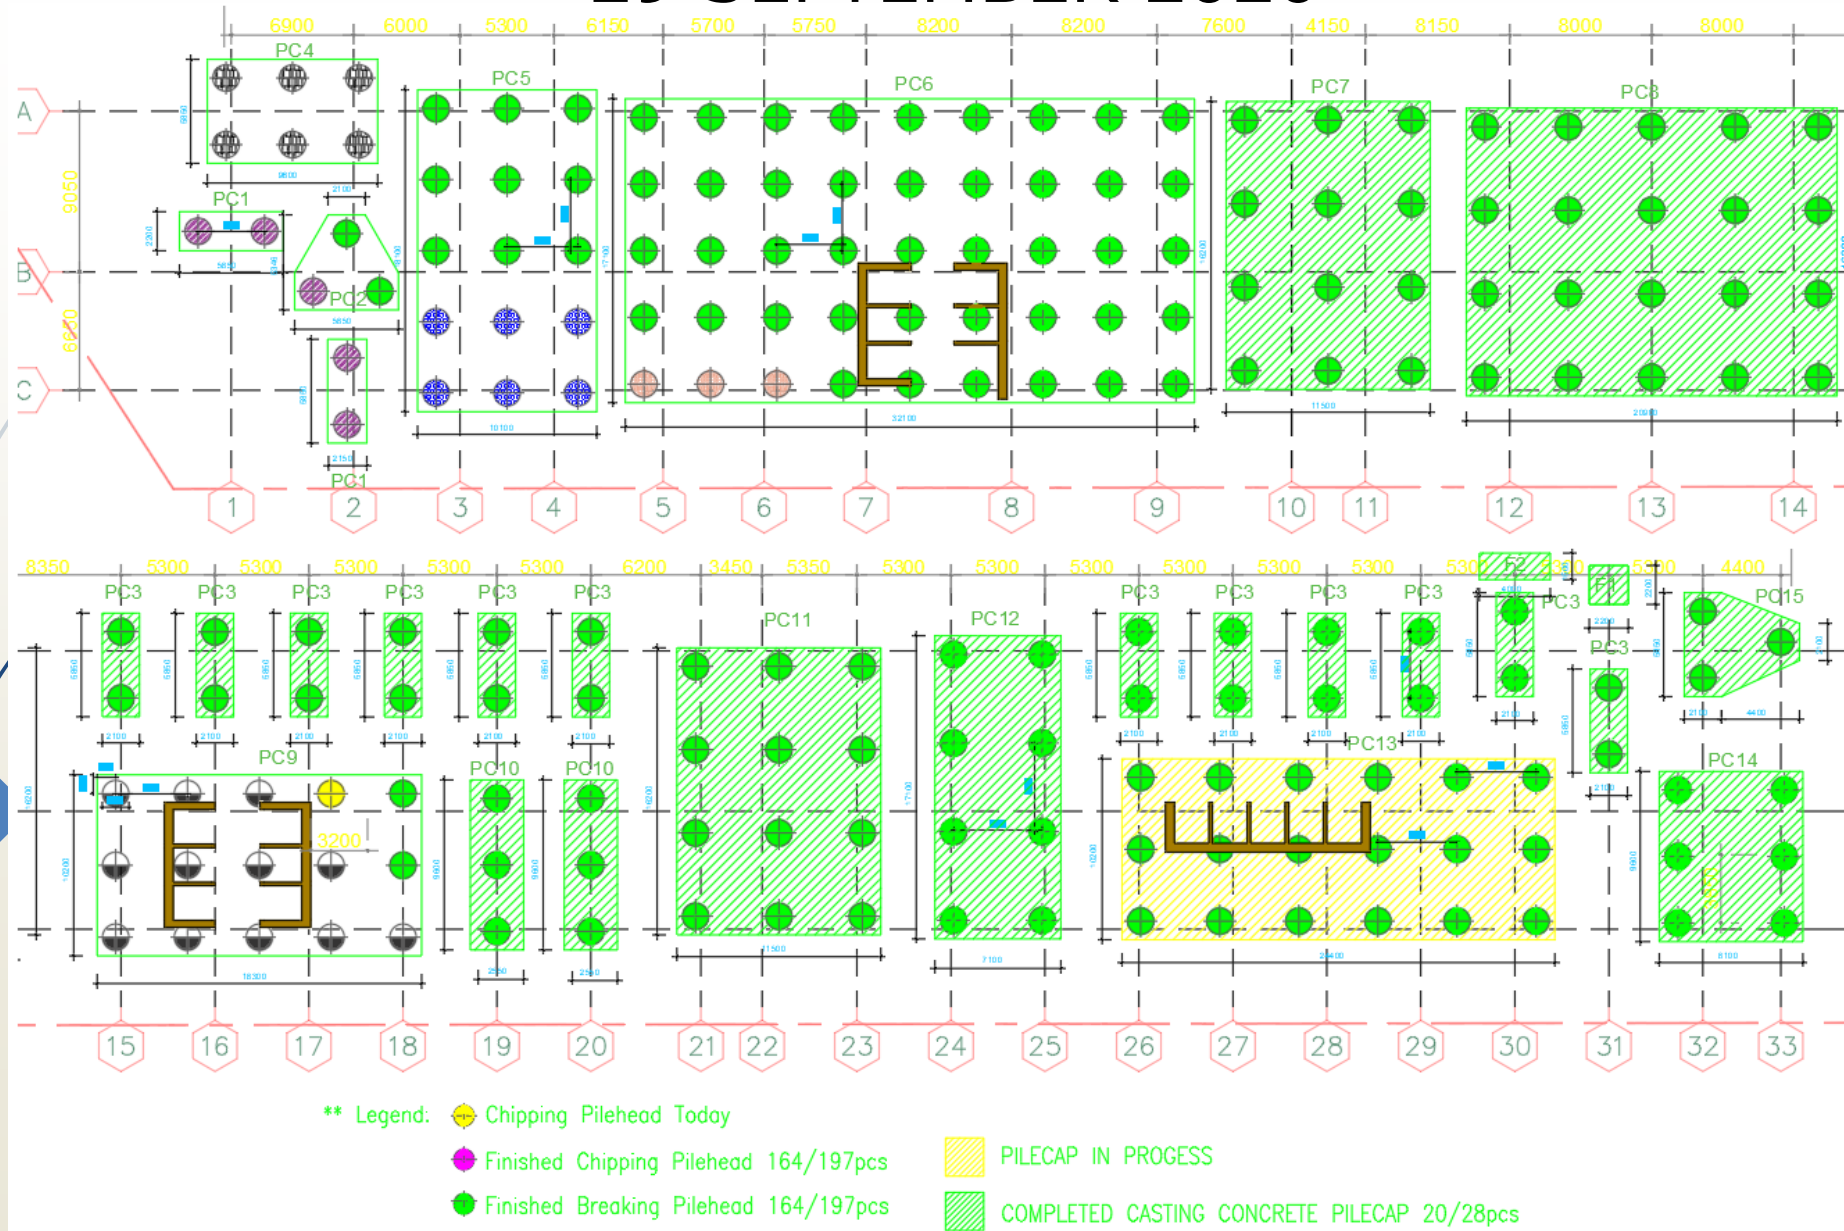

SOIL EXCAVATE FOR PC2, PC9 & PC13



CHIPPING PILE-HEAD PC2 & PC9



REBAR WORK FOR PC6 & PC13



INSTALLING GROUNDING SYSTEM



SOIL BACKFILL PC10, PC11 & PC12



SOIL DEPOSAL




SITE ENVIRONMENT





PASSION FOR PROGRESS!



TIME SQUARE 10 OCEAN VIEW

THE BEST DAY IN OTRES BEACH

THANK YOU!
