



Time Square

Time Square 11 — Report

29. AUG. 2026



Weekly Report





Time Square 11



PROJECT LOCATION





Time Square 11


Time Square 11 Point Of View





Time Square 11

Time Square 11 Point Of View

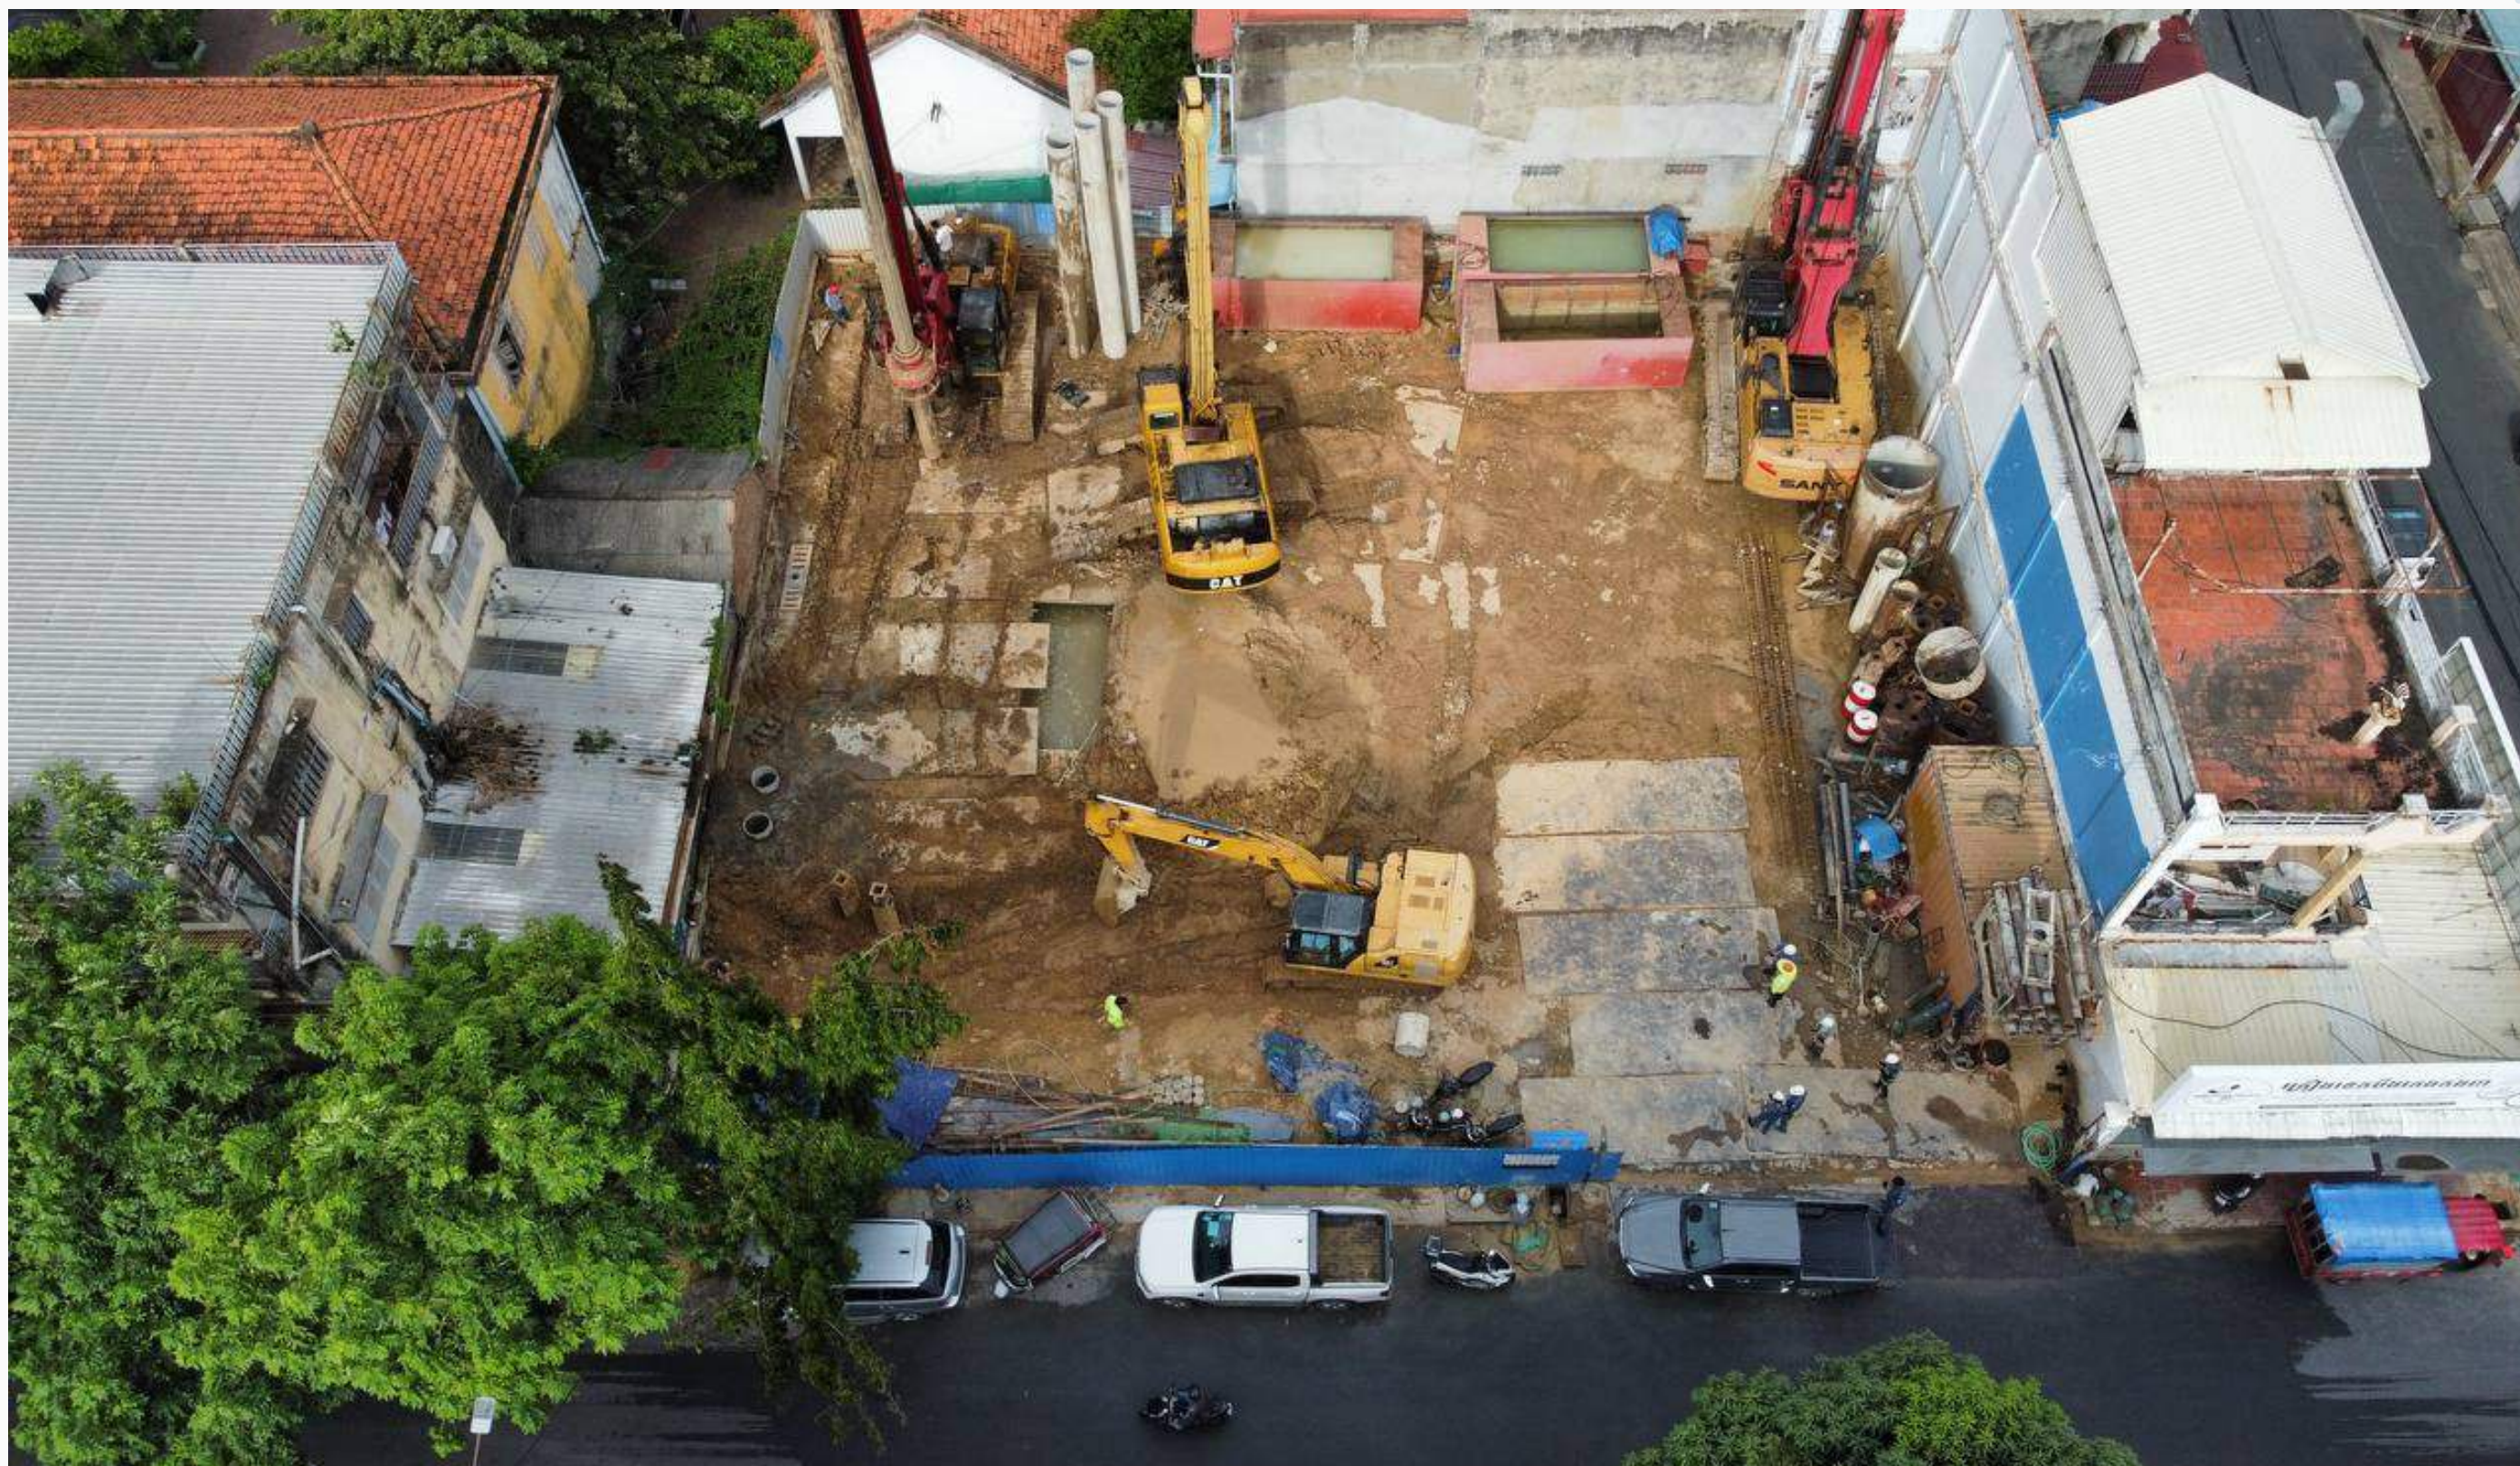





Time Square 11

CBP PROGRESS

CBP PILES (168/168 PILES)



Done
100%

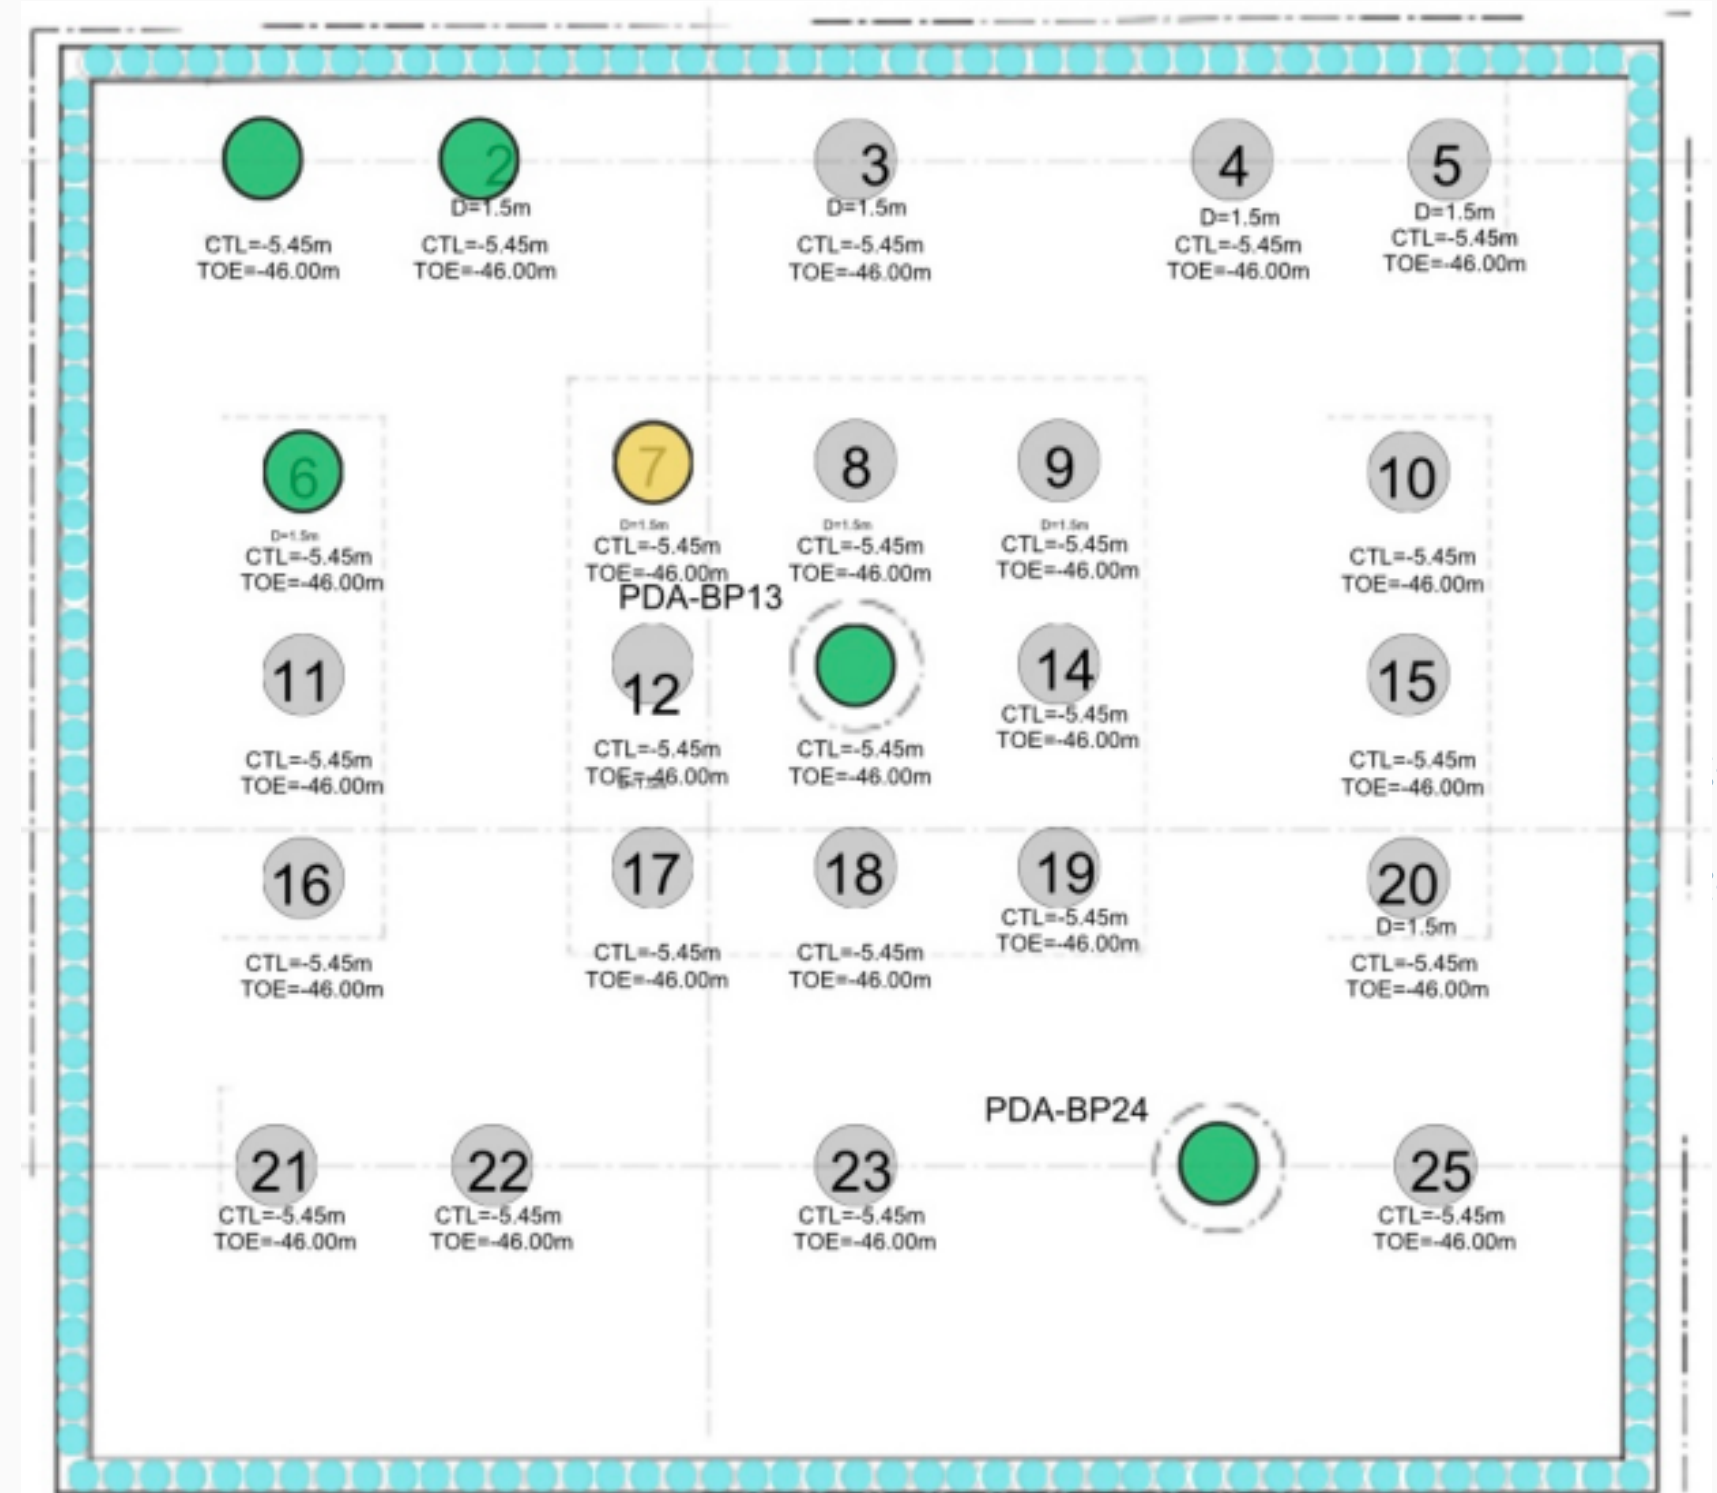





Time Square 11

PDA Test Progress

PDA PROGRESS (2/2 Piles)

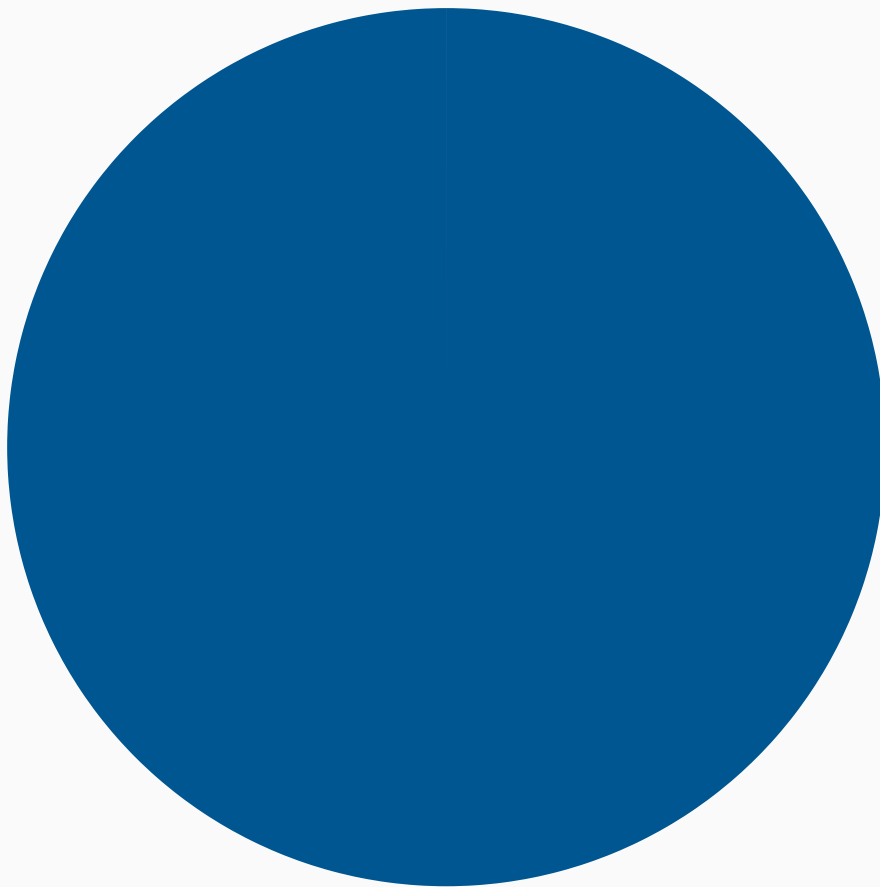

Done
100%

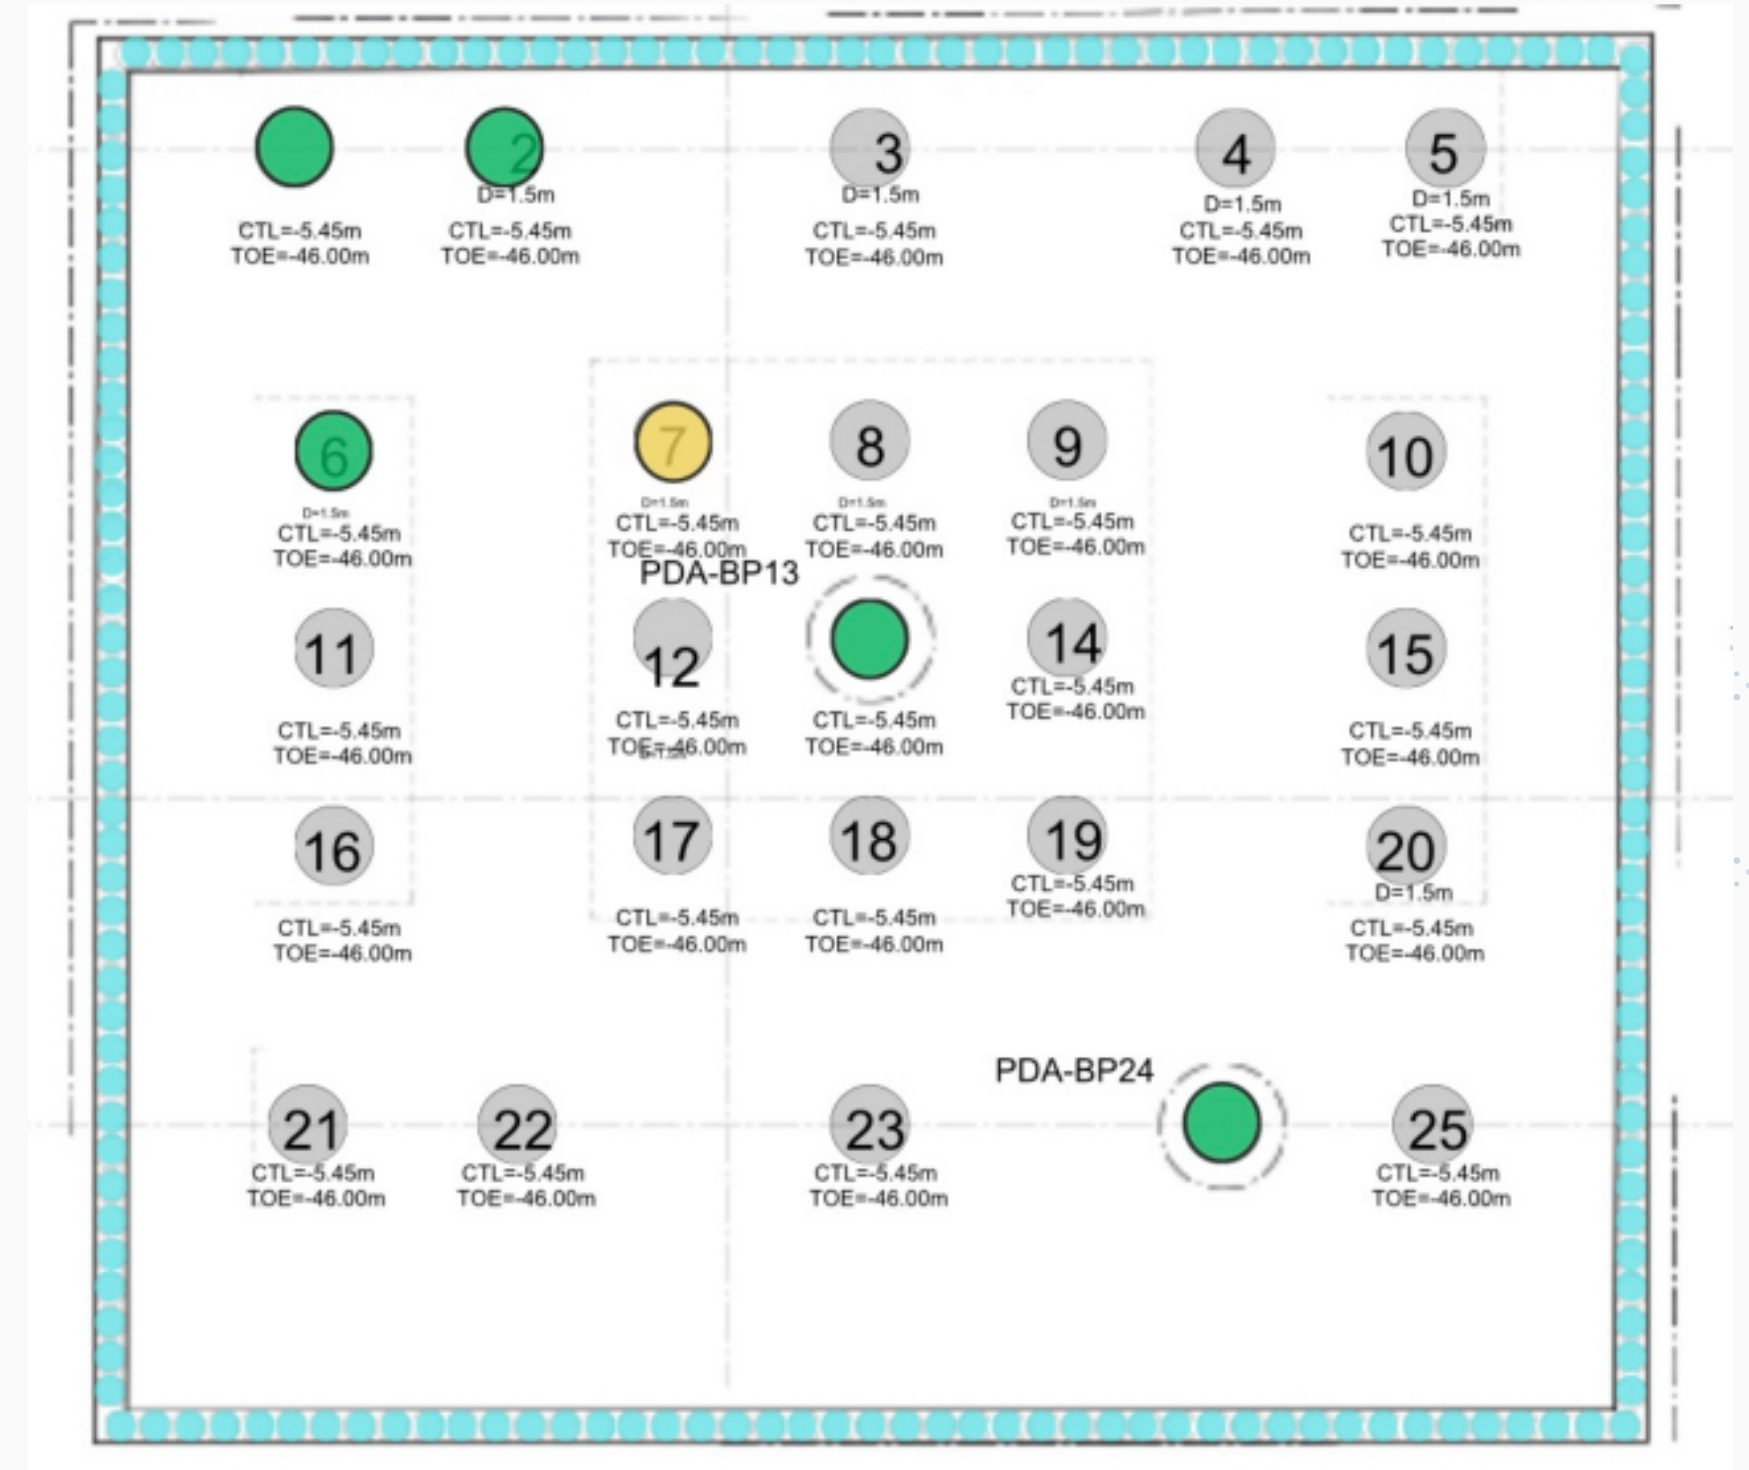




Time Square 11


Cross-hole Sonic Progress

Up to 29. AUG. 2026 (02/25 Piles)

Sonic Test PROGRESS

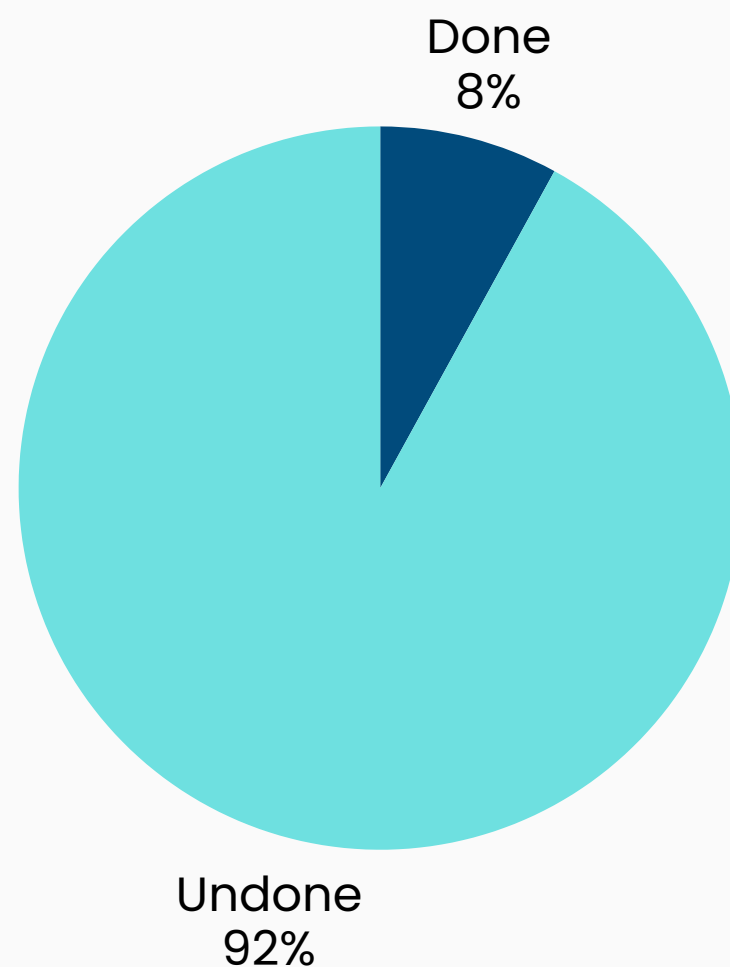

Finished Sonic testing.

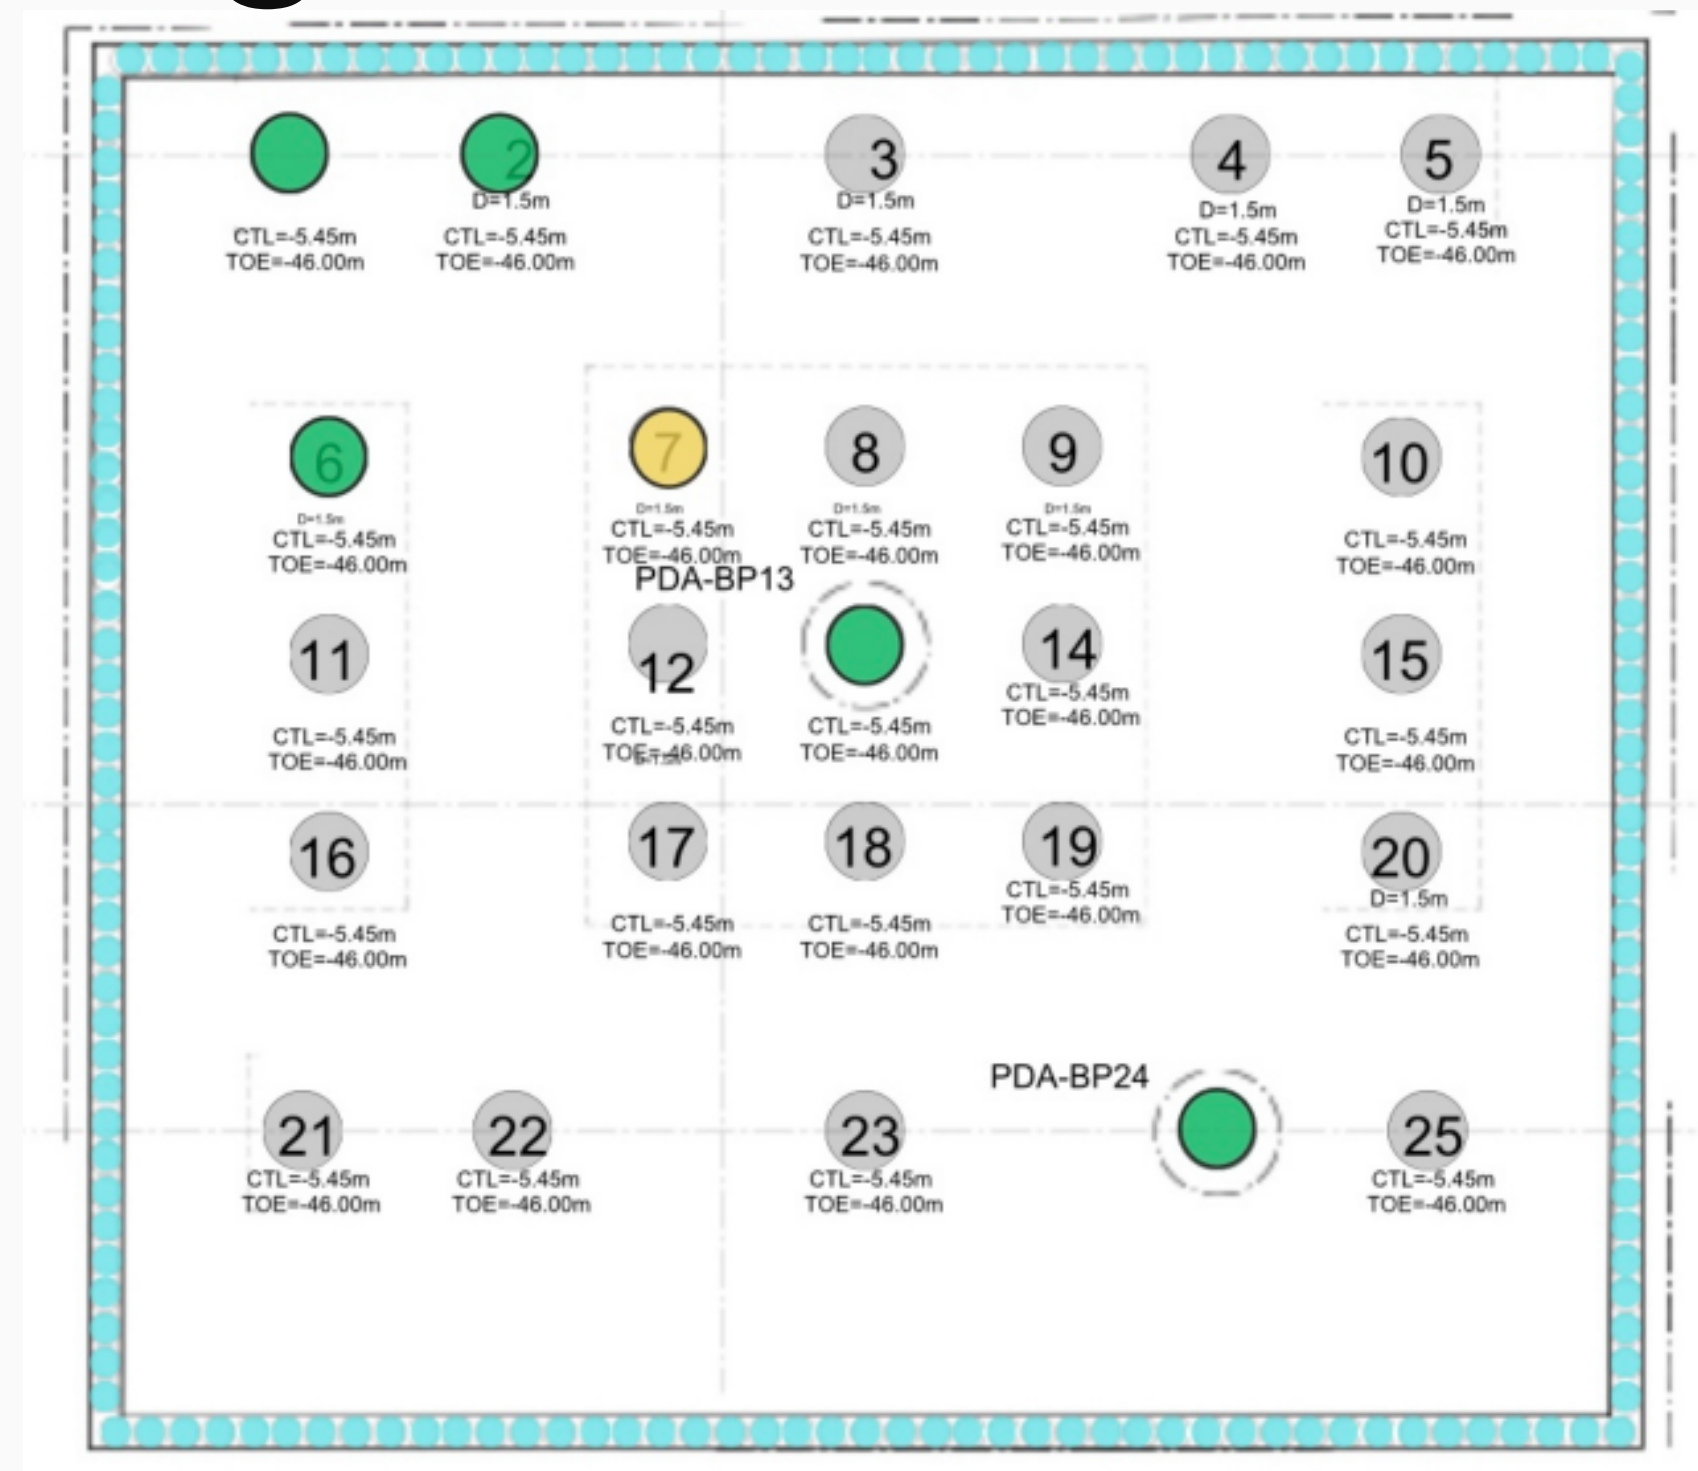




Time Square 11


Main Pile Progress

Up to 29. AUG. 2026 (05/25 Piles)

Main Pile PROGRESS

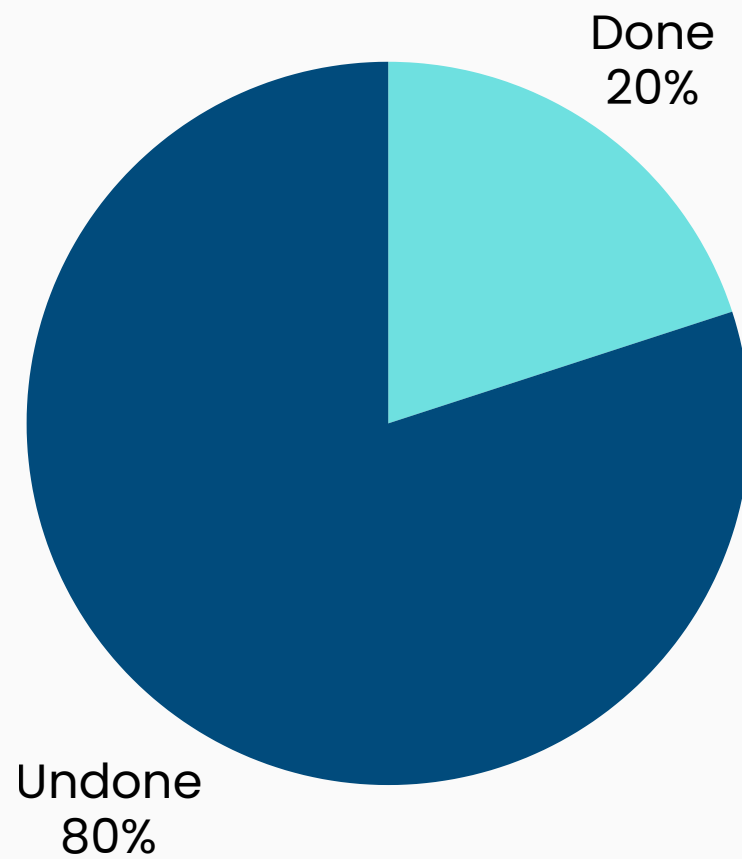

-  Finished Main Pile Concrete.
-  Unfinished Main Piles.

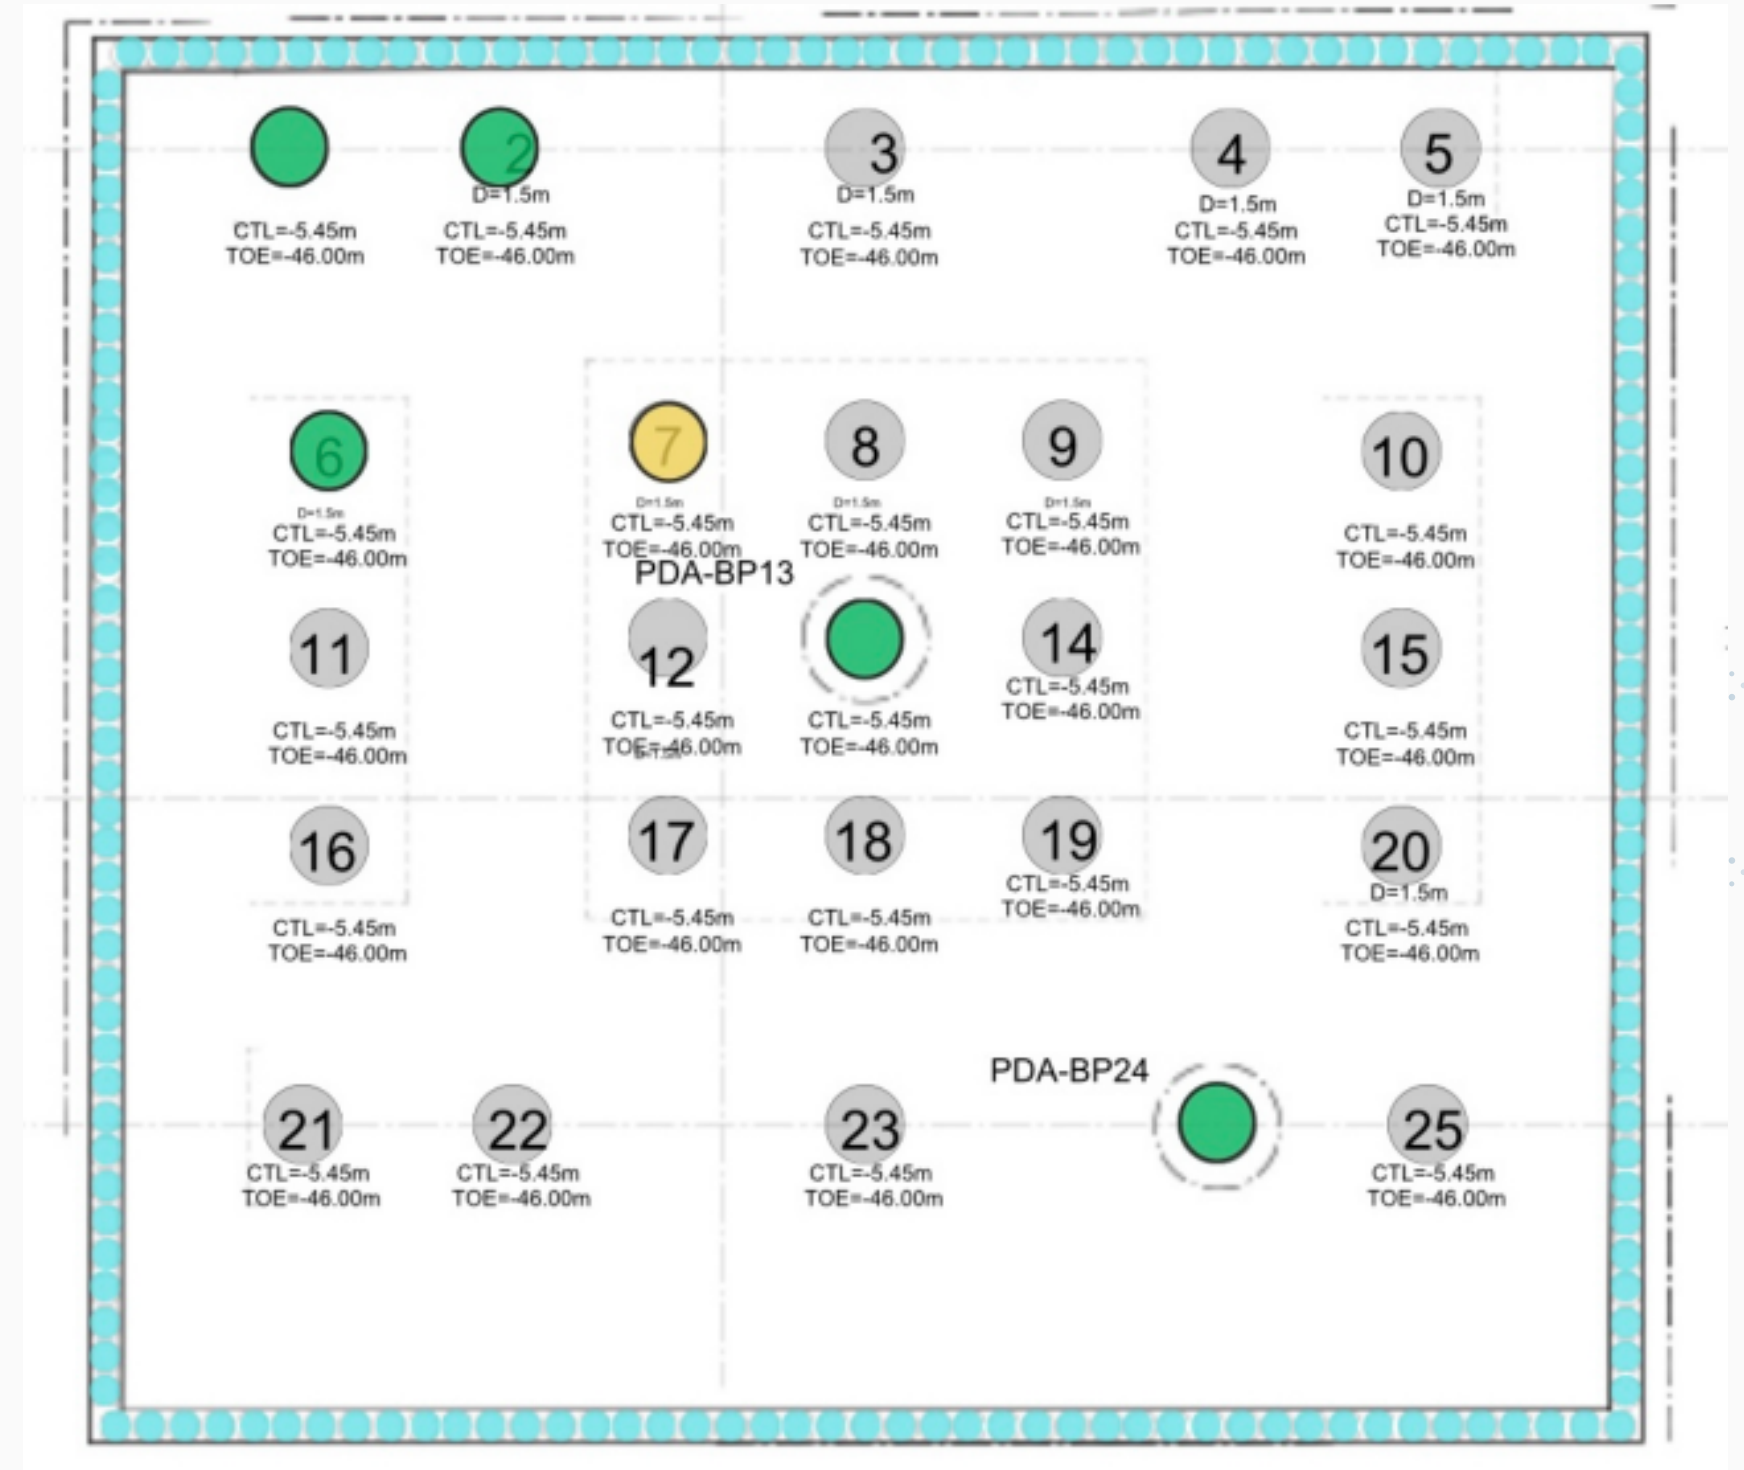



Time Square 11

Drilling Work





Time Square 11

Coordinate Inspection




Pile ID: BP-02, BP-06, BP-07



Time Square 11

Bentonite Inspection

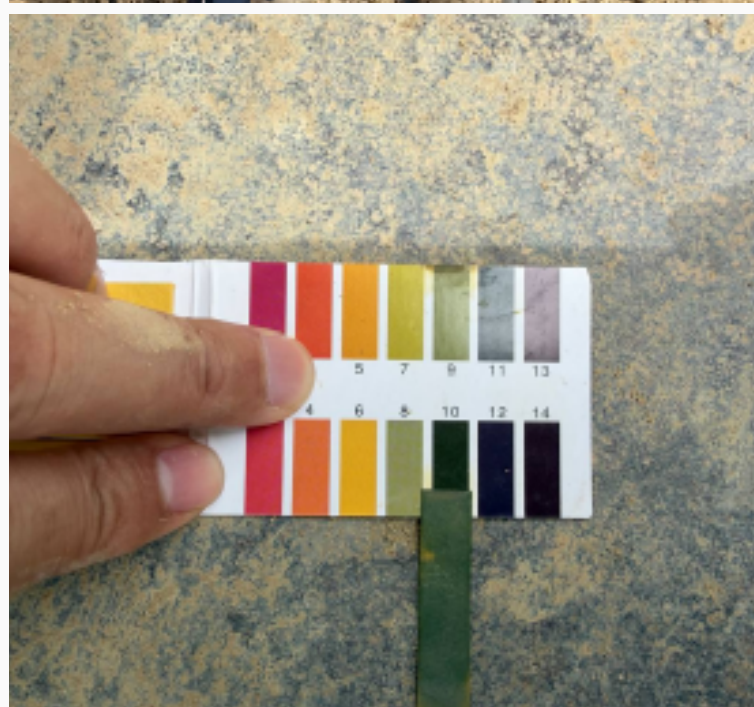



Time Square 11

Rebar Inspection





Time Square 11

Depth Inspection / Lowering Rebar





Time Square 11

Slump Inspection





Time Square 11

Site Cleaning





Time Square 11

Passion For Progress!

Thank You!

